



# Certificate of Completion

## Duct Sealing Performed For:

kroloffs, noah  
4113 49th st nw  
washington, dc 20016

## Overall Sealing Results

When we arrived,  
YOUR DUCTS HAD:

**418.4 CFM of Leakage**, equivalent to a  
**79.0 Square Inch Hole**


*This equals 251 refrigerators full of air loss every hour.*

After we finished,  
YOUR DUCTS HAVE:

**10.1 CFM of Leakage**, equivalent to a  
**1.9 Square Inch Hole**

This corresponds to a **97.6% Reduction in Duct Leakage.**

Note: Duct Leakage results are calculated in Cubic Feet per Minute (CFM) measured at a standard OPERATING PRESSURE of 25 Pa.

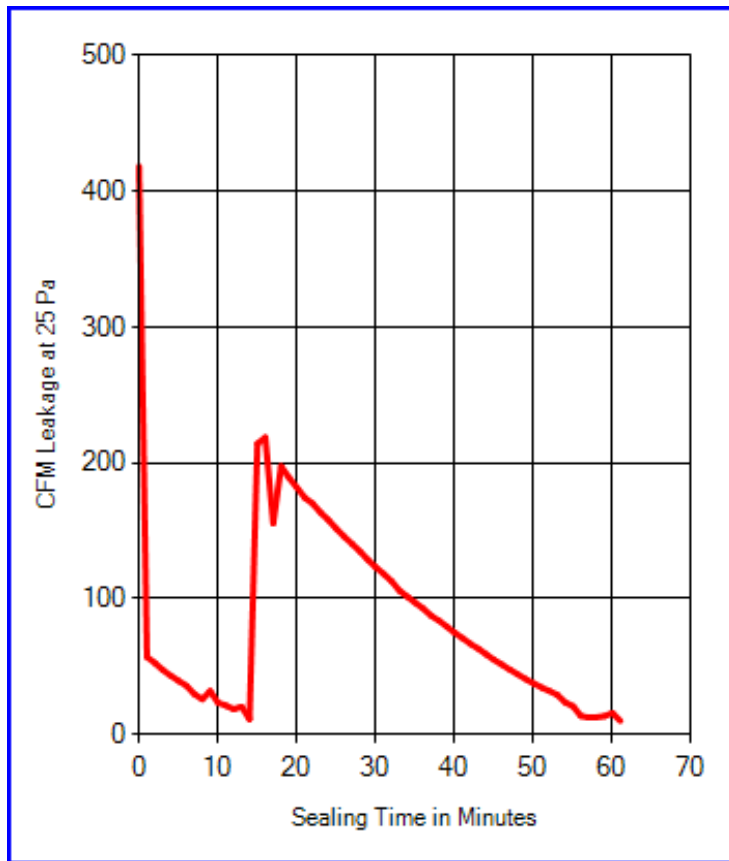

Aeroseal Technician **brian**

Aeroseal Case ID **4174**

Date of Seal **9/19/2017**

System Description **forced air**

Seal Description **2&3rd floor**

Hardware **HomeSeal**

## Duct Sealing Performed By:

James A. Wheat & Sons, Inc.  
7834 Beechcraft Ave.  
Gaithersburg, MD 20879  
Phone: 301-670-1944

**AEROSEAL**<sup>®</sup>  
Duct Sealing From The Inside
